

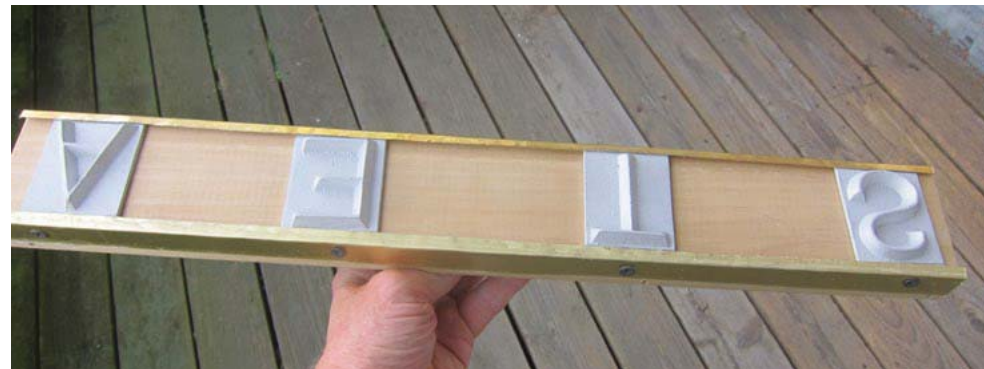


Concrete Poetry Impressions: Permanent Installation Implementation Steps


1. Contractor will stamp text in pavement along alignment at selected locations.
2. Artist Team will purchase stamp sets and provide to Contractor.
3. Artist Team will coordinate with Contractor to define how best to set the stamps.
4. Contractor to implement a mock-up/example stamping prior to construction.
5. Artist Team will provide stamp holders that are able to hold a full line of text.
6. Artist Team will coordinate with Contractors on stamp setting and may ready stamps in holders prior to Contractor stamping.
7. Total estimated amount of text per section
 - a. West side: 38 locations
 - b. East side north: 64 locations
 - c. East side south: 27 locations
8. Text specifications
 - a. Letter height is to be 2"
 - b. 50 characters maximum per text box, including spaces.
 - c. Spacing of letters will be determined by the physical letter sets.
 - d. Alignment of letters will be determined by the wood letter holders.
 - e. Distance between lines will be 2 1/2" (to be confirmed after physical mock-up)
 - f. Text and writing will stay within scoring patterns as set by project at each location. Staying within scoring patterns provides a 'page' for the writing.
9. Margins created for the 'page' will be 6" from the top and 4" from the left.
10. Artist Team will provide Contractor with layout/typesetting templates for each location of poetry.

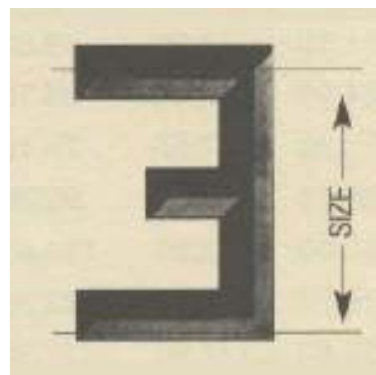

CONCRETE POETRY STAMPING DETAILS

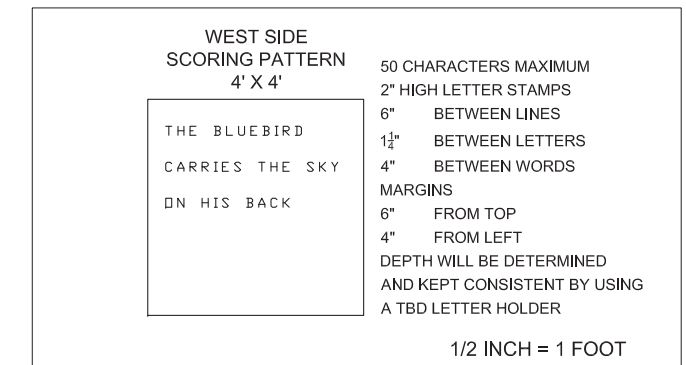

DETAIL 1/ART8

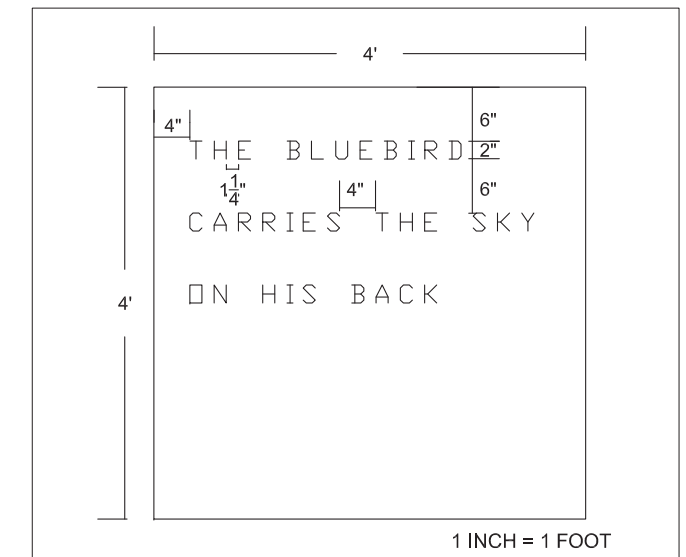

DETAIL 2/ART8

